ID	Task Name	Start	Duration	Finish
0	EIA - SIA and Resettlement	Oct 03	90.4 wks	Aug 12
1	**Pre-application phase**	**Oct 03**	**68.4 wks**	**Mar 09**
2	Initialise project	Oct 03	1 wk	Oct 07
3	Compile and submit pre-application meeting request	Oct 10	5 days	Oct 14
4	Consultation with DEA	Nov 16	1 day	Nov 16
5	Compile application form	Jun 16	5 days	Jun 22
6	Client review and acceptance	Jun 23	3 days	Jun 27
7	Submit EIA application form to DEA in SA and Botswana	Jun 28	2 days	Jun 29
8	SA DEA Acknowledgement and issuing of case reference numt	Jul 10	1 day	Jul 10
9	SA DEA Timeframe: submit Scoping Report by	Aug 13	1 day	Aug 13
10	SA DEA Timeframe: submit EIAr by	Mar 09	1 day	Mar 09
11	**Scoping Phase**	**Oct 17**	**50.8 wks**	**Oct 30**
12	Draft SEP and BID	Oct 17	21 days	Nov 14
13	Client Review of SEP and BID	Nov 15	19 days	Dec 09
14	Client review and acceptance	Dec 09	0 days	Dec 09
15	Circulate BID for comment and advertise	Dec 09	0 days	Dec 09
16	PPP: review period	Dec 10	50 days	Jan 29
17	Comment and Response Document	Dec 08	20 days	Jan 27
18	Draft Scoping Report (DSR)	May 08	6 wks	Jun 16
19	Scoping Stakeholder Engagement Documents	Jun 16	0 days	Jun 16
20	Alternative route from Watershed B location confirmed	May 24	0.2 wks	May 24
21	Client Review and acceptance of DSR and SE docs	Jun 16	0 days	Jun 16
22	Incorporate Client Review Comments, print & courier	Jun 26	3 days	Jun 28
23	Draft scoping report for PPP	Jun 29	1 day	Jun 29
24	Public Comment Period - DSR	Jun 30	33 days	Aug 01
25	Public Meeting -DSR (if required)	Jul 14	5 days	Jul 20
26	Final Scoping Report (FSR) & CRR	Aug 03	1 day	Aug 03
27	Peer review of Scoping Report	Jul 07	20 days	Aug 03
28	Client Review and acceptance of FSR & CRR	Aug 04	4 days	Aug 09
29	Incorporate Client Comments	Aug 10	5 days	Aug 16
30	Missed Deadline - 30day public participation proces	Aug 16	4.4 wks	Sep 14
31	Submit FSRs (print and courier)	Sep 14	0 days	Sep 14
32	Final Scoping Report to DEA in SA and Botswana	Sep 15	1 day	Sep 15
33	Authority Review Period (including decision on PoS for EIA)	Sep 15	46 days	Oct 30
34	Acceptance of Scoping Report and PoS	Oct 30	0 days	Oct 30
35	**Specialist Studies**	**Jun 07**	**8.8 wks**	**Aug 07**
36	Site visit	Jul 03	5 days	Jul 07
37	**Specialist studies**	**Jun 07**	**4.6 wks**	**Jul 07**
38	Avifauna (Chris van Rooyen)	Jun 07	1.15 mons	Jul 07
39	Biodiversity (Brian Collity)	Jun 07	1.15 mons	Jul 07
40	Climate Change (Aurecon)	Jun 07	4.6 wks	Jul 07
41	Heritage (Stephen Gaigher)	Jun 07	4.6 wks	Jul 07
42	Socio-economic (Aurecon)	Jun 07	4.6 wks	Jul 07
43	Visual (Aurecon)	Jun 07	4.6 wks	Jul 07
44	Specialists report reviews and finalisation	Jul 10	10 days	Jul 21
45	Final Specialist reports	Jul 24	6 days	Jul 31
46	Summarise and intergrate reports	Aug 01	5 days	Aug 07
47	**EIA Phase**	**Aug 08**	**49.6 wks**	**Aug 12**
48	Draft EIA Report and EMP	Aug 08	4.6 mons	Dec 13
49	EIA Stakeholder Engagement Documents	Dec 13	0 days	Dec 13
50	Client Review and acceptance of Draft EIR & EMP and SE doc	Dec 14	5 days	Jan 11
51	Incorporate Client Review Comments, print & courier	Jan 12	6 days	Jan 19
52	Draft EIA Report	Jan 22	2 days	Jan 23
53	PPP Advertisement appears	Jan 25	0 days	Jan 25
54	Public Comment Period (Draft EIR)	Jan 26	32 days	Feb 26
55	Public Meeting - EIR (if required)	Feb 13	4 days	Feb 16
56	Final EIR & EMP	Feb 27	5 days	Mar 05
57	Peer review of EIA Report	Feb 06	20 days	Mar 05
58	Client Review and acceptance	Mar 08	2 days	Mar 09
59	Incorporate Client Comments, Print & Courier	Mar 12	2 days	Mar 13
60	Submit Final EIA Report to DEA	Mar 14	1 day	Mar 14
61	Authority Review Period	Mar 15	112 days	Jul 04
62	Decision	Jul 04	0 wks	Jul 04
63	Notify I&Aps of decision	Jul 21	1 day	Jul 21
64	Appeal period	Jul 21	23 days	Aug 12
65	**Botswana EIA**	**Nov 01**	**32.2 wks**	**Jul 05**
66	Stakeholder Comments follow-up	Nov 01	2 wks	Nov 14
67	Compile scoping and TOR	Nov 01	10.6 wks	Feb 05
68	Submitt Scoping and TOR to DEA	Feb 05	0 wks	Feb 05
69	DEA Review of Scoping and TOR	Feb 06	12 days	Feb 21
70	DEA approval of scoping and TOR	Feb 21	0 days	Feb 21
71	Compile Draft EIA Report	Jan 18	3.6 wks	Feb 12
72	Internal & Client review	Feb 13	12 days	Feb 28
73	Finalise Draft EIA report	Mar 01	5 days	Mar 07
74	Submitt draft EIA report to DEA	Mar 08	1 day	Mar 08
75	DEA Review and allocate service providers (60 Days as per EIA	Mar 09	2.2 mons	May 09
76	Make final Adjustments based on comments from DEA	May 10	11 days	May 24
77	Submitt final EIA to DEA	May 24	0 days	May 24
78	DEA final review period	May 25	5 days	May 31
79	Receive approval on Final EIA	May 31	0 wks	May 31
80	**Public Participation process**	Jun 01	5 wks	Jul 05
81	Prepare PPP materials	Jun 01	1 wk	Jun 07
82	Place advertisments	Jun 01	0 wks	Jun 01
83	Public review and comment period	Jun 08	4 wks	Jul 05
84	DEA approval	Jul 05	0 wks	Jul 05
85	**RAP**	**Nov 14**	**60.6 wks**	**Feb 26**
86	Socio-economic survey of project impacts and affected populati	Aug 01	2 mons	Sep 25
87	Legal /policy framework for land acquisiton and compensation	Nov 14	2.6 wks	Nov 30
88	Inventory of assets and Infrastructures	Jul 10	2.8 mons	Sep 25
89	Establishment of Compensation framework	Jan 10	3.2 wks	Jan 31
90	Establishment of framework for livelihood restoration and Devel	Sep 26	2.2 wks	Oct 10
91	Prepare Implementation Schedule & budget	Sep 26	8.8 wks	Nov 24
92	Organisational responsibilities for Implementation and budgets	Oct 02	8 wks	Nov 24
93	Develop dispute resolution and grievance redress mechanisms	Oct 02	8 wks	Nov 24
94	Develop framework for consultation, participation and development planning	Oct 02	8 wks	Nov 24
95	Develop framework for monitoring, evaluation and reporting	Oct 02	8 wks	Nov 24
96	Draft RAP Report	Nov 27	5 wks	Jan 22
97	RAP finalisation	Jan 23	4.8 wks	Feb 23
98	Final RAP Report	Feb 26	1 day	Feb 26

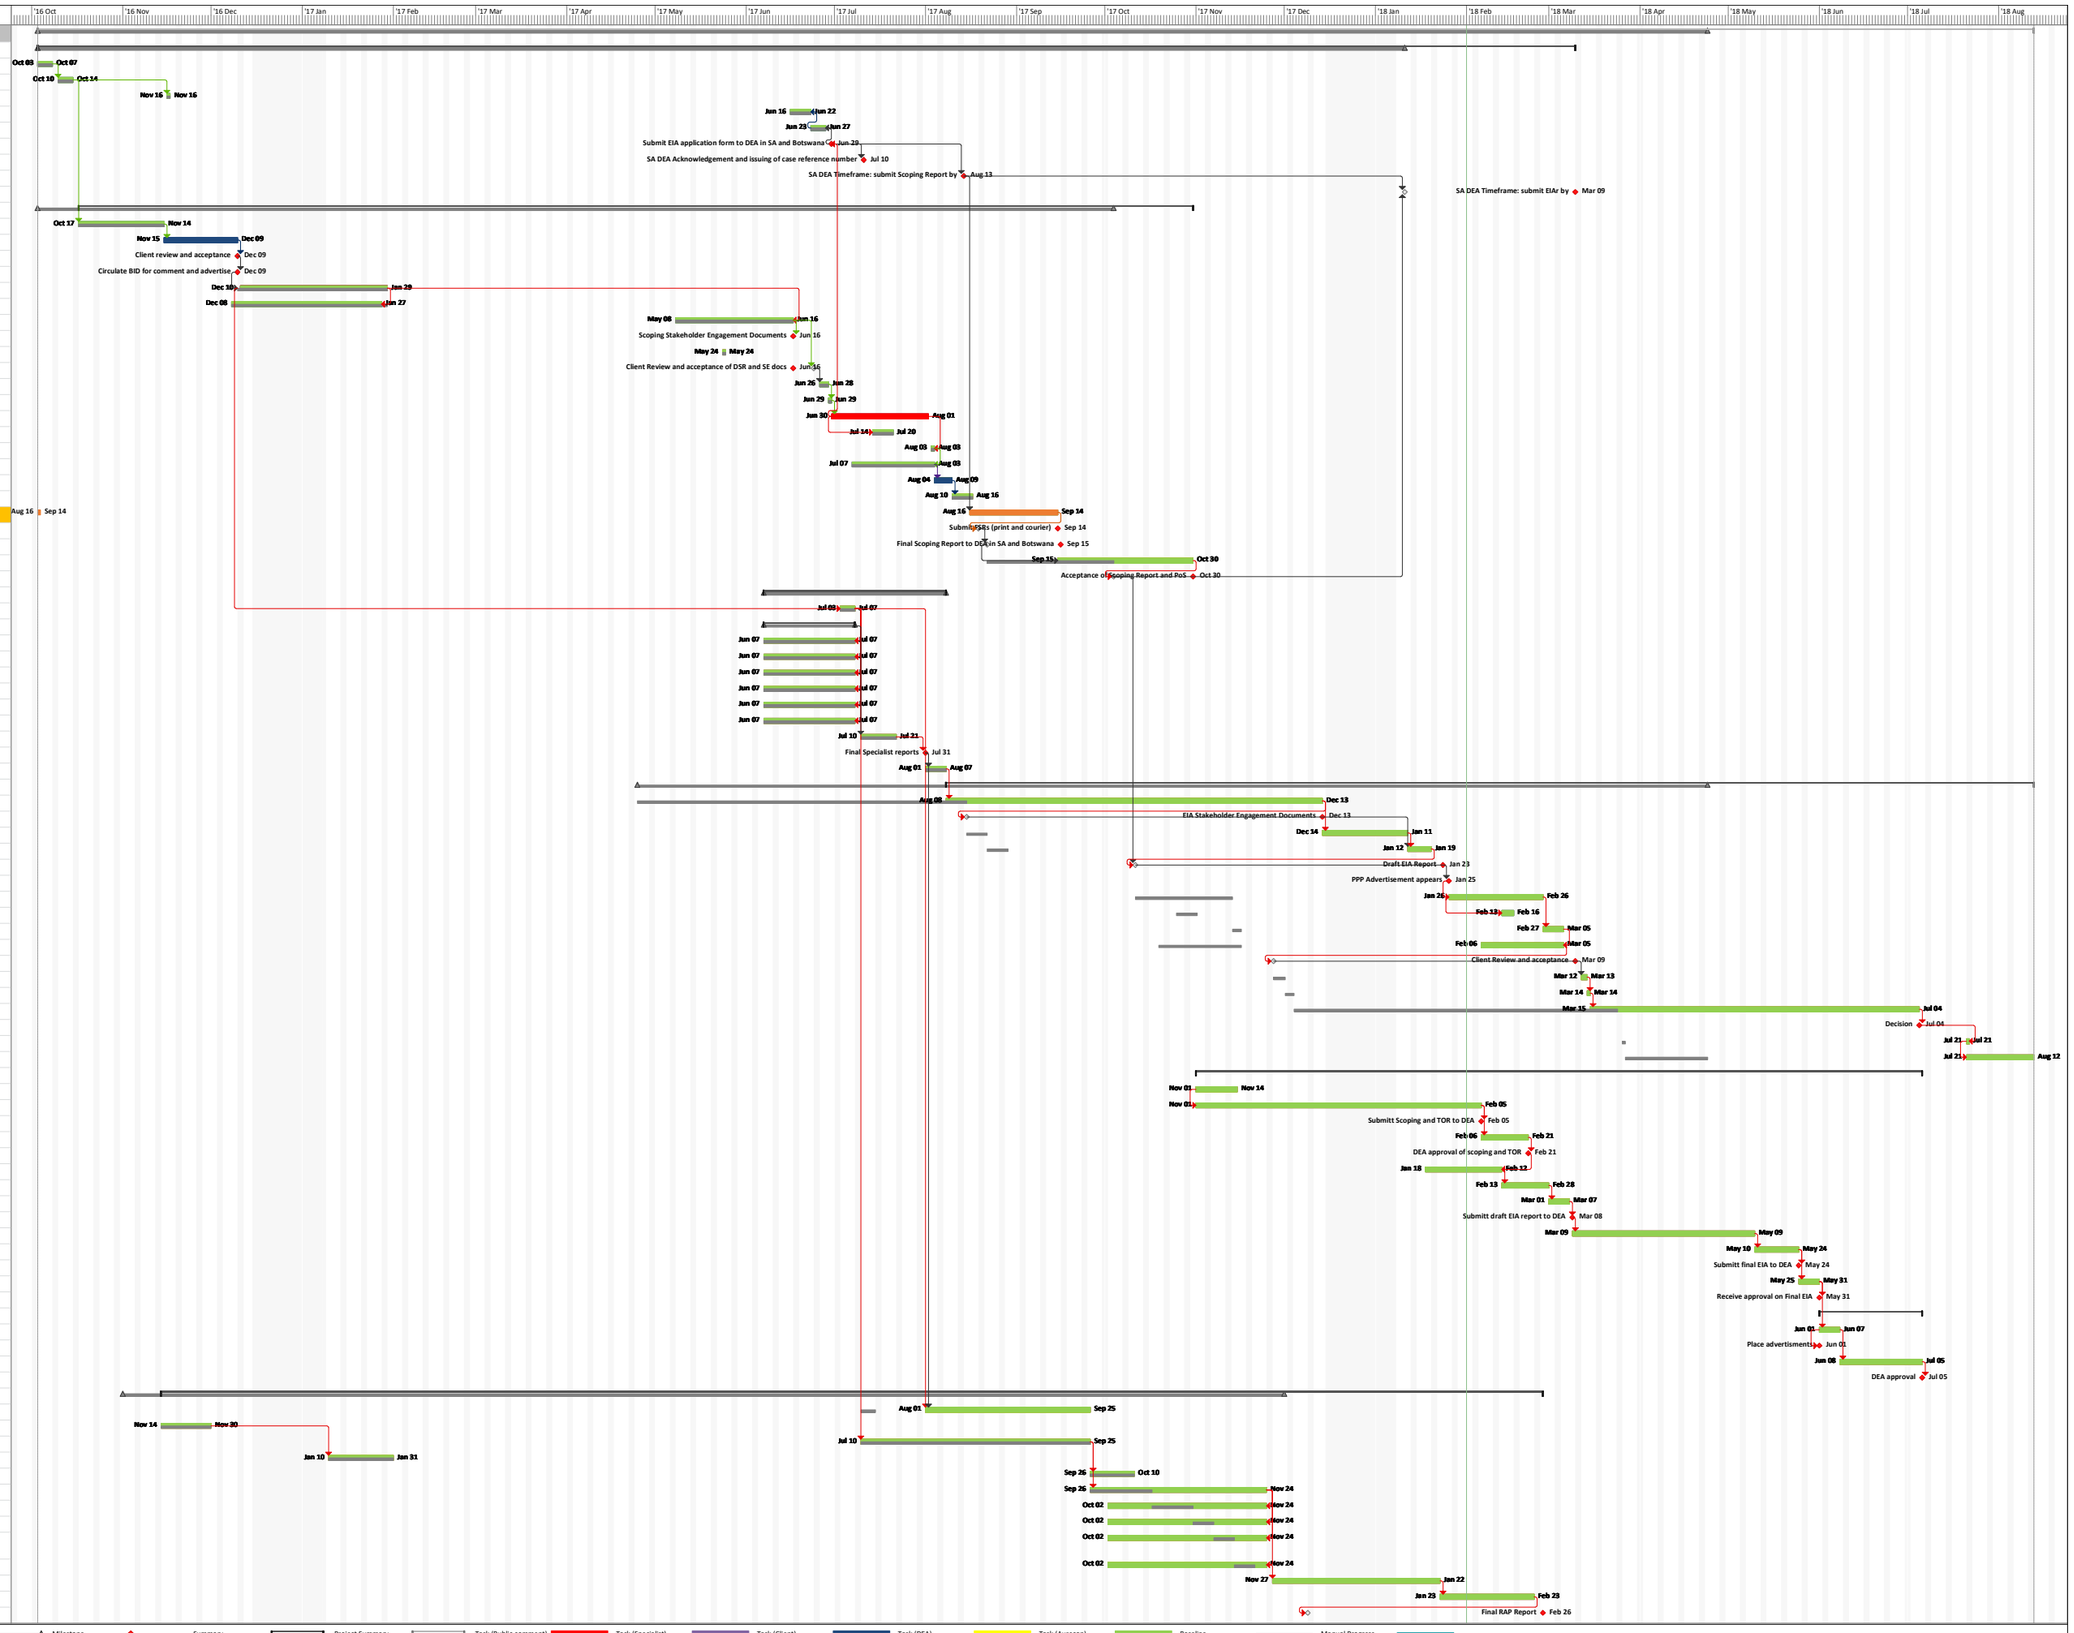

Project: EIA - SIA and Resettlemen
Date: Feb 01

Baseline Milestone | Baseline Summary | Milestone | Summary | Project Summary | Task (Public comment) | Task (Specialist) | Task (Client) | Task (DEA) | Task (Aurecon) | Baseline | Manual Progress
